



Week in Review and Lookahead

Friday, February 26, 2021


GLT's **diversity** is **representative** of the communities we serve as we strive each day to transform the Green Line for all of our riders. As Black History Month comes to a close, the GLT Team Story for this week is from our dedicated **Deputy Chief, Desiree Patrice**, whose principled leadership and commitment to excellence are integral to the GLT program. Desiree shared about her professional path and her personal insights on how to bring your best to your work. [Read more about Desiree](#), as well as [Horace Cooper](#) and [Tamiaka Thibodeaux](#), in the GLT Team Stories featured during Black History Month. Looking ahead to March, GLT is excited to share design plans for making [Symphony Station](#) fully accessible! Join our [virtual public meeting](#) on March 3 at 6:00 p.m. to learn more.



Rise.

Desiree Patrice
GLT Deputy Chief

B Branch Station Consolidation


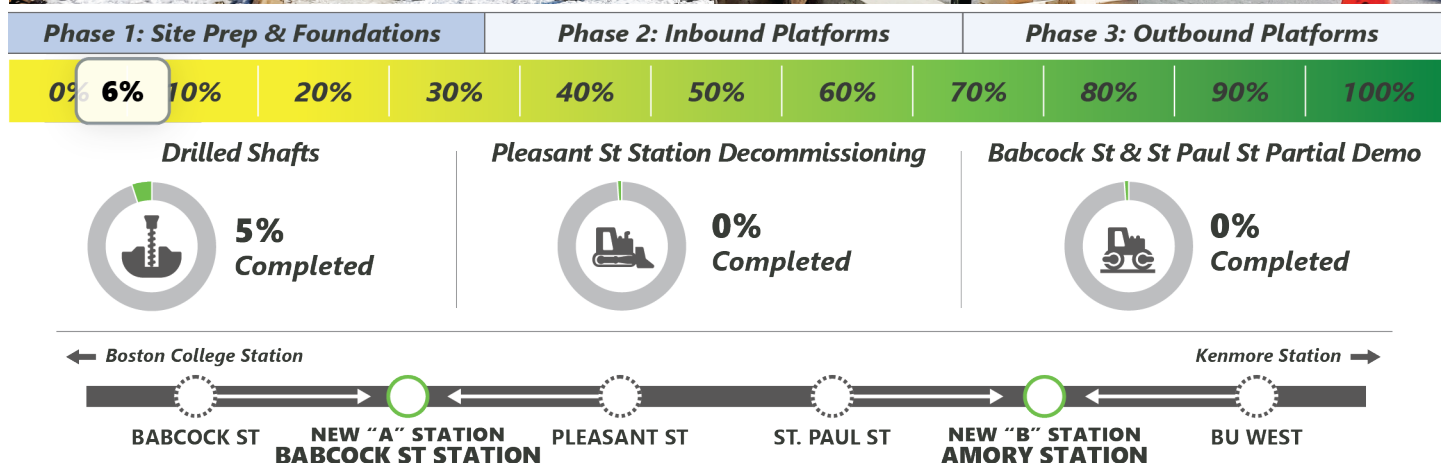


Consolidate four (4) existing Green Line stations on the B Branch along Commonwealth Avenue adjacent to Boston University, into two (2), fully accessible, brand new stations (Babcock & Amory)

- ✓ **Last Week** | Crews began drilling shafts for the foundation of the new Amory St. Station between St Paul and BU West
- **Lookahead** | Pleasant St. Station will be decommissioned over the weekend. Crews will continue to drill shafts and install electrical conduits for the new Amory St. Station

**Schedule subject to change with weather conditions and in accordance with public health directives*

Lechmere Viaduct Rehabilitation Project

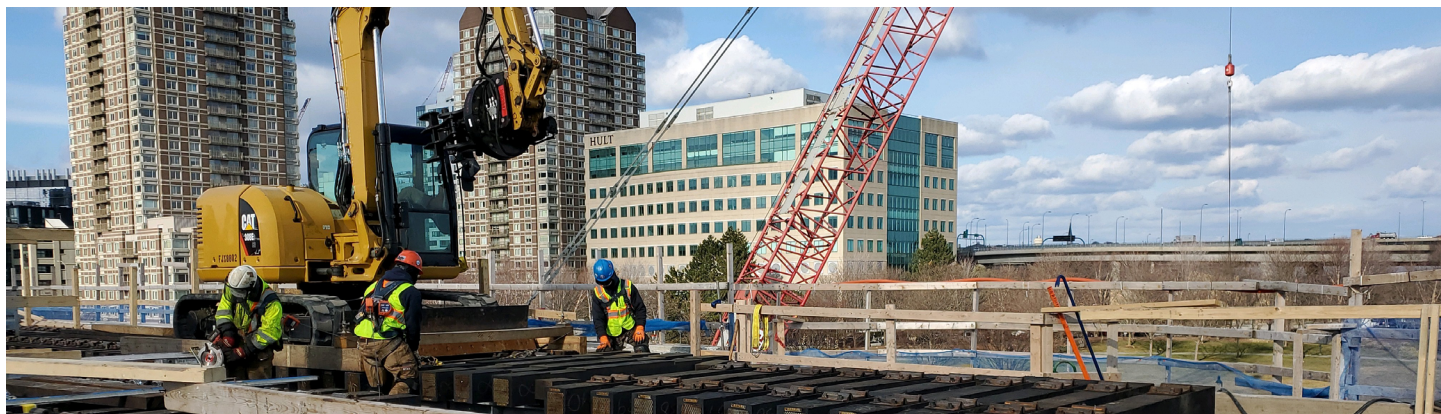

1,700 ft of Structural Repairs Underway (12 Spans)



Trackwork




29%
Completed

Signal



5%
Completed

Power



10%
Completed

Concrete & Structural



67%
Completed

Strengthen and preserve the 110-year-old viaduct for heavier loads and increased train frequency

- ✓ **Last Week** | Work continued on the interior of Piers 5, 6 & 7 - the contractor installed rebar into existing concrete and regouted to structurally strengthen the piers
- **Lookahead** | Contractor will continue repainting the steel bascule span as well as continuing with the timber tie installation and structural repairs to piers

**Schedule subject to change with weather conditions and in accordance with public health directives*

Alternative Service

B Branch Alternative Service | February 15 – March 5, 2021

B Branch shuttles buses replace service between Babcock St and Kenmore Stations weeknights after 8:45 PM and all day on weekends

Learn more about the B Branch service changes at [diversions/green-line-b](#)

E Branch Alternative Service | E Branch shuttle buses replace service between North Station and Lechmere until Spring 2021 to allow for work on the Green Line Extension and the Lechmere Viaduct Rehabilitation Project

Learn more about the E Branch service changes at [diversions/green-line-e](#)

